

# Winchester Center Station Accessibility Improvements: Construction Update

Public Information Meeting

June 25, 2024

Nathan Rae, MBTA Senior Project Manager

### Thank You for Participating!

- Thank you for joining the meeting! We appreciate your participation.
- This meeting will be recorded so that it can be shared it with the people that were unable to join.



### Diversity and Civil Rights

#### **English**

All MBTA activities, including public meetings, are free of discrimination. The MBTA complies with all federal
and state civil rights requirements preventing discrimination on the basis of race, color, national origin,
limited English proficiency, and additional protected characteristics. We welcome the diversity from across
our entire service area. If you have any questions or concerns, please visit <a href="www.mbta.com/titlevi">www.mbta.com/titlevi</a> to reach
the Office of Diversity and Civil Rights.

#### Spanish

Todas las actividades de MBTA, incluidas las reuniones públicas, están libres de discriminación. La MBTA cumple con todos los requisitos de derechos civiles federales y estatales que impiden la discriminación por motivos de raza, color, origen nacional, dominio limitado del inglés y características protegidas adicionales.
 Damos la bienvenida a la diversidad de toda nuestra área de servicio. Si tiene alguna pregunta o precupacion, visite www.mbta.com/titlevi para comunicarse con la Oficina de Diversidad y Derechos Civiles.

#### Chinese

• MBTA 的所有活动,包括公开会议,都没有歧视。 MBTA 遵守所有联邦和州公民权利要求,防止基于种族、肤色、国籍、有限的英语能力和其他受保护特征的歧视。我们欢迎来自我们整个服务领域的多样性。如果您有任何问题或疑虑,请访问 www.mbta.com/titlevi 联系多元化和民权办公室


#### **Closed Captions**


Click Closed Caption to start viewing closed captioning

**Tip:** Click and drag the closed captioning to move its position in the meeting window.

#### To adjust the caption size:

- Click the upward arrow next to Start Video / Stop Video.
- Click Video Settings then Accessibility.
- Move the slider to adjust the caption size







### Use the Chat for Technical Questions

#### **English**


If you have a technical question about Zoom or the features of the meeting, please use the chat function. Our technical assistant labeled "Winchester Station Project Team" will attempt to troubleshoot your problem and get back to you.

#### **Spanish**

Si tiene una pregunta técnica de zoom o los enseres de zoom durante la junta. Favor de usar el chat. Nuestro asistente técnico bajo el nombre de "Zoom Tech" le ayudará con su problema.

#### Chinese

如果您有关于**Zoom**或者会议功能的技术问题,请使用对话框的聊天功能。我们的技术辅助员会回复您并尽力帮您解决问题。



### Agenda


- Project Overview
- Recent Construction Activity
- Schedule Impacts
- Schedule Impact Mitigation
- Schedule Update
- Upcoming Construction
- Project Contacts



#### **Project Overview**

- Full Station Reconstruction:
  - Two new fully accessible, high-level, side platforms with canopies.
  - Three new elevators, two new ramps and three sets of covered stairs.
  - New lighting, signage and wayfinding, security cameras, and other amenities.
  - New tracks, ties, ballast, bridge plates and communication duct banks.
- Total Construction Cost: \$50 Million



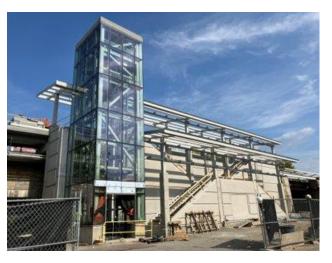

### Recent Construction Activity, Spring 2024



Laraway Road stair installation



Waterfield Lot side of the Headhouse



Aberjona ramp


### Recent Construction Activity, Spring 2024



Platform and stairway at the Aberjona side of the Headhouse



View of the Station along Laraway Road

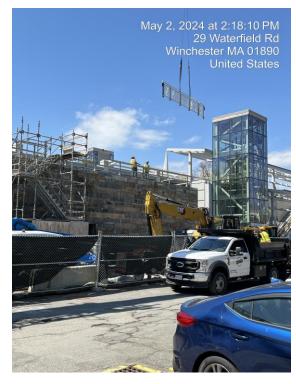

Guardrail installation at Aberjona side of the Headhouse

#### Schedule Impacts

- Schedule Impacts:
  - Lost ability to single track and went to foul time (from March 6 to May 8).
    - ATC/PTC Program
    - Fiber Optic Resiliency Project
    - North side Commuter Rail Maintenance work
  - Support resources constrained by system wide project demand.
    - Track Improvement Program
    - GLX
    - SCR



#### **Project Schedule Updates**

Winchester Station is now scheduled to partially reopen by September 30, 2024. Partial reopening in September includes:


- Partial platform reopening on the south half of the station inbound and outbound platforms with one elevator for each platform (2 total).
- Return of parking in Aberjona and Waterfield lots.
- Completion of work on Waterfield Road.
- Substantial completion and the full station reopening are scheduled for December 2024.
- Punch list work and landscaping are scheduled for 2025.

### Schedule Impact Mitigation

- Schedule Impact Mitigation
  - Altered train schedule reduced mid-day train service for additional construction access (March)
  - Reschedule for and maintenance work (May)
  - Restored single tracking (May).
  - Added work crews
  - Added work shifts: weekends and nights (as needed)
  - Extended normal hours



## Sequence of Opening, Parking Restoration

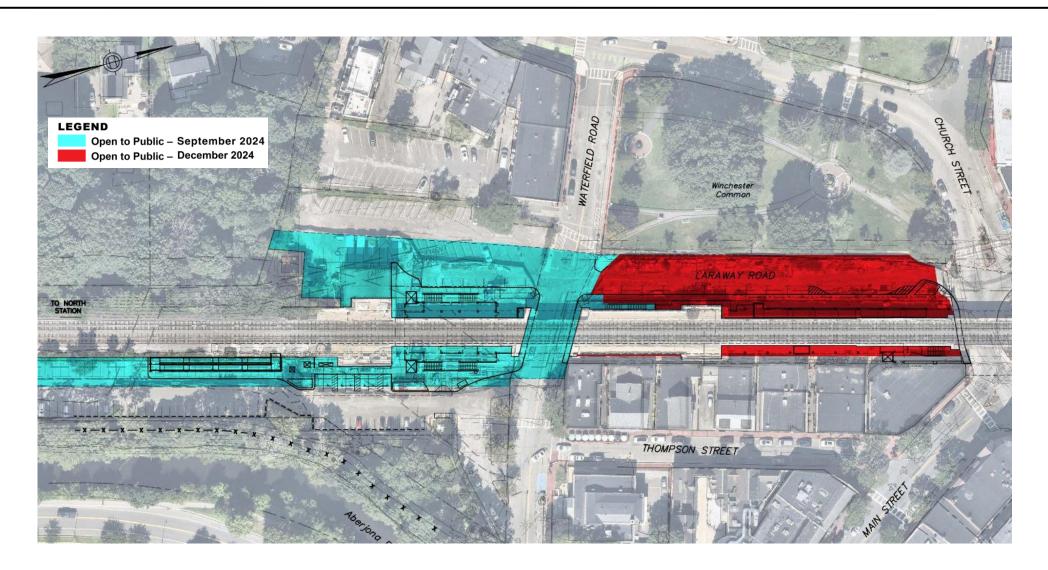

#### Upcoming Construction: What To Expect this Summer/Fall 2024

- Continued steel, electrical, concrete, and plumbing work:
  - Focusing on the south end of station on both the east and west headhouses, Aberjona ramp and Mid Stair on Laraway, and inbound and outbound platforms.
  - Steel work, elevator, and staircase construction on the north end of the station.
  - Neighbors can expect continued noise from construction activity including heavy equipment and machinery.
- Requests for night work are forthcoming. The MBTA intends to limit nightwork as much as possible. Construction advisories will be distributed ahead of any scheduled night or weekend work.

# Upcoming Construction – Summer/Fall 2024

Activity	May	June	July	Aug.	Sept.	Oct.	Nov.	Dec.
Platform Level - FRP Platform panels, Canopy Steel, Electrical, Lighting, Communications, Station Signage, VMS, Benches,								
<ul> <li>Aberjona and Waterfield Sections:</li> <li>Headhouse Elevator Construction</li> <li>Plumbing, Electrical, Communications</li> <li>Stairways, Construct FRP Platform and Ramp placement</li> <li>Parking lot restoration</li> </ul>								
Behind Thompson Street & Quill Rotary Sections: - Plumbing, Electrical, Structural Steel - Communications, Elevator, Stairs, FRP Platform - Construction of Rotary Pier								
<ul> <li>Laraway Section:</li> <li>Construct Ramps, Platform &amp; Stairway, Structural Steel,</li> <li>Utility installation</li> </ul>								

#### **Project Contact Information**

- Project Email Address:
   winchesterstation@MBTA.com
- Construction Hotline: (781) 218-9717
  For construction-related concerns and questions.
- Project Website:
   www.mbta.com/winchesterstation



#### Raising Your Hand

- Please use Zoom's "Raise Hand" feature to indicate if you have a comment
  - All participants are muted upon entry so that only the presenters can be heard. Please raise your hand and the meeting host will ask you to unmute so that you can state your question/comment.
- Por favor de usar el encero de levantar la mano en Zoom para indicar que usted tiene algún comentario o pregunta.
  - Todos los participantes en esta llamada están silenciados, para que solo los presentadores se puedan oír. Cuando usted levante su mano, manda un alerta a la moderadora que quisiera hablar. La moderadora le quitará el silencio para que pueda hacer su pregunta o comentario.
- 如果您有评论,请使用 Zoom 的"举手"功能。
  - 所有的参与者在进来时都被静音了以便于只听到演讲者。请举手,会议主持人将让您取消静音,以便您陈述您的问题/评论。







