





# Week in Review and Lookahead

Friday, March 5, 2021

For GLT, **keeping connected** with our riders is always a priority. Since the onset of the pandemic, we have developed new strategies to stay connected in a virtual way and be proactive in communicating with riders and neighbors of the Green Line through virtual public meetings, weekly email updates, social media posts, and frequent website updates. This week, we held a **virtual public meeting** for the 75% design plans for the Symphony Station Accessibility Improvements project. The meeting was recorded and is available [online](#) if you were not able to listen in.



## B Branch Station Consolidation

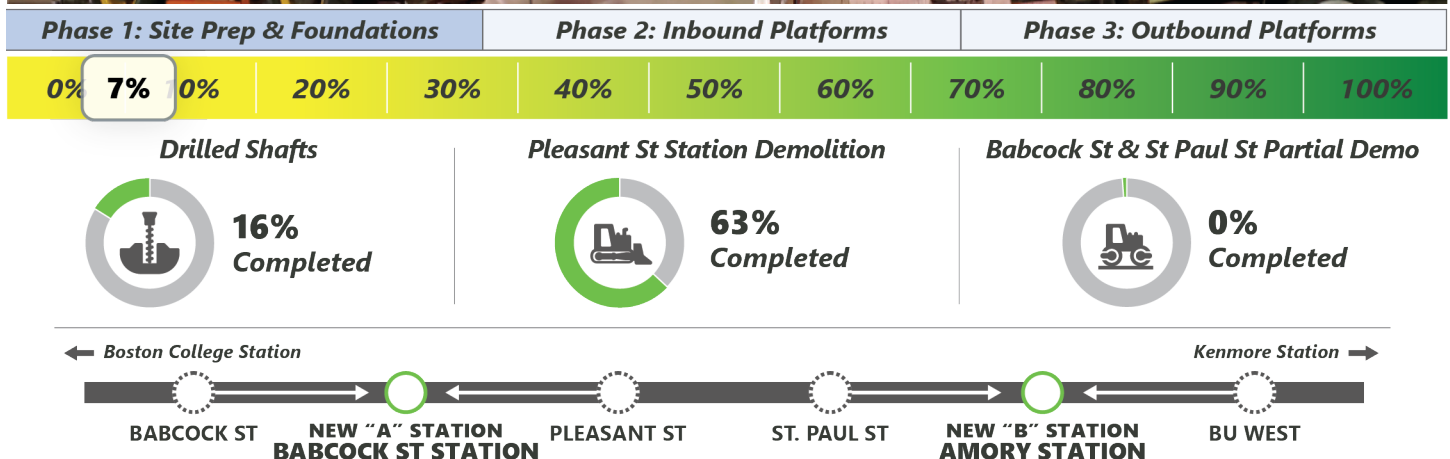

Consolidate four (4) existing Green Line stations on the B Branch along Commonwealth Avenue adjacent to Boston University, into two (2), fully accessible, brand new stations (Babcock & Amory)


- ✓ **Last Week** | Pleasant St. Station was decommissioned over the weekend. Crews continued to drill shafts and installed electrical conduits for the new Amory St. Station
- **Lookahead** | Crews will be continuing installation of the drilled shafts, installation of electrical conduit, and final demolition of Pleasant St. Station. Crews will also begin utility work at Babcock St. Station

\*Schedule subject to change with weather conditions and in accordance with public health directives

# Lechmere Viaduct Rehabilitation Project



## 1,700 ft of Structural Repairs Underway (12 Spans)



### Trackwork




**30% Completed**

### Signal



**5% Completed**

### Power



**10% Completed**

### Concrete & Structural



**68% Completed**

Strengthen and preserve the 110-year-old viaduct for heavier loads and increased train frequency

- ✓ **Last Week** | Contractor continued repainting the steel bascule span as well as continued with the timber tie installation and structural repairs to piers
- **Lookahead** | Crews will focus on installing timber ties at spans 1 and 2 as well as continuing concrete and rebar work to rebuild and strengthen exterior walls


*\*Schedule subject to change with weather conditions and in accordance with public health directives*

## Alternative Service

### B Branch Alternative Service | March 5 – 19, 2021

B Branch shuttle buses replace service between Babcock St and Kenmore Stations weeknights after 8:45 PM and all day on weekends, except for Fridays, March 5, 12, 19 and the weekends of March 6 – 14 when shuttles operate from Washington St. to Kenmore.

Learn more about the B Branch service changes at [diversions/green-line-b](#)



**E Branch Alternative Service** | E Branch shuttle buses replace service between North Station and Lechmere until Spring 2021 to allow for work on the Green Line Extension and the Lechmere Viaduct Rehabilitation Project

Learn more about the E Branch service changes at [diversions/green-line-e](#)

