

## Winchester Center Station Accessibility Improvements: Construction Update

Town of Winchester Select Board Meeting

March 28, 2022

Nathan Rae, Sr. Project Manager, MBTA Capital Delivery

## Agenda

- Project Overview
- Spring/Summer Construction Schedule
- Upcoming Construction
- Traffic & Parking Impacts
- Transit Alternatives
- Public Outreach



## **Project Overview**


- Full Station Reconstruction:
  - Install new elevators and stairs
  - Install fully accessible, high-level side platforms
  - Covered stairwells and upgrade sidewalk
  - New emergency lighting and security cameras
  - > Updated station and wayfinding signage
- Total Estimated Construction Cost: \$48 Million



# Spring/Summer Construction Schedule


2022	Schedule	Status
<b>Preconstruction:</b> Preconstruction surveys, permit applications, construction submittals, etc.	February – March 2022	Completed
<ul> <li>Site Preparation:</li> <li>Equipment brought on site.</li> <li>Implement Traffic Management Control, Parking restrictions &amp; Pest Control Plan.</li> <li>Installation of temporary fencing &amp; utility relocations</li> <li>Environmental controls established</li> </ul>	Starting in late March	Upcoming
<b>Demolition Phase at Aberjona Lot:</b> Mobilization at Aberjona Lot: work to be done on ground level and platform level of station	End of April through May 2022	Future
<b>Demolition Phase at Waterfield Lot:</b> Mobilization at Waterfield Lot: work to be done on ground level and platform level of station	June through August 2022	Future

### Upcoming Construction: Aberjona Lot

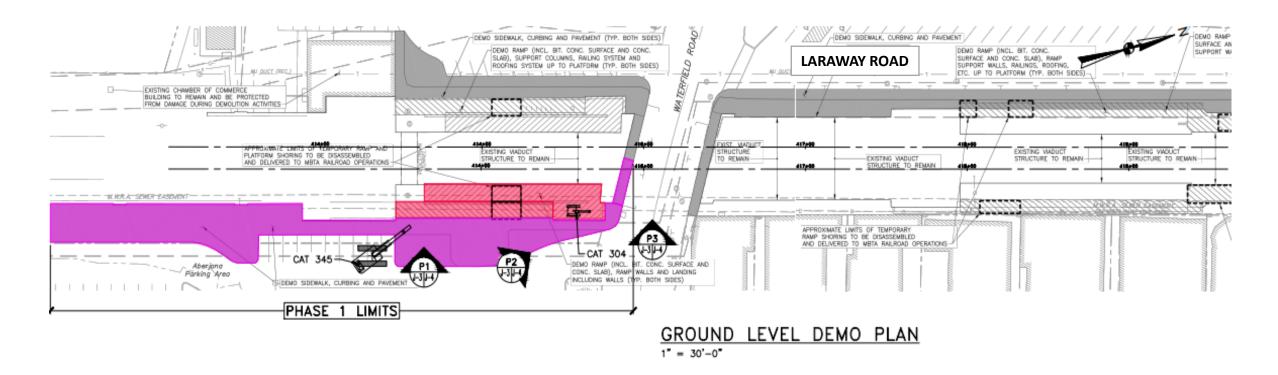


- Construction crew to mobilize on site at the end of April
- Work will continue through May 2022

## Upcoming Construction: Waterfield Lot

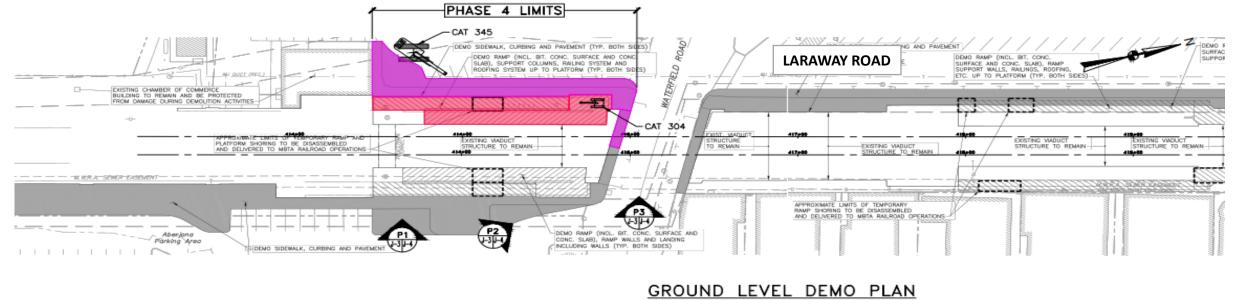


- 1" = 30'-0"
- Construction crew to mobilize on site in early June 2022
- Work will continue through August 2022

### **Traffic & Parking Impacts**

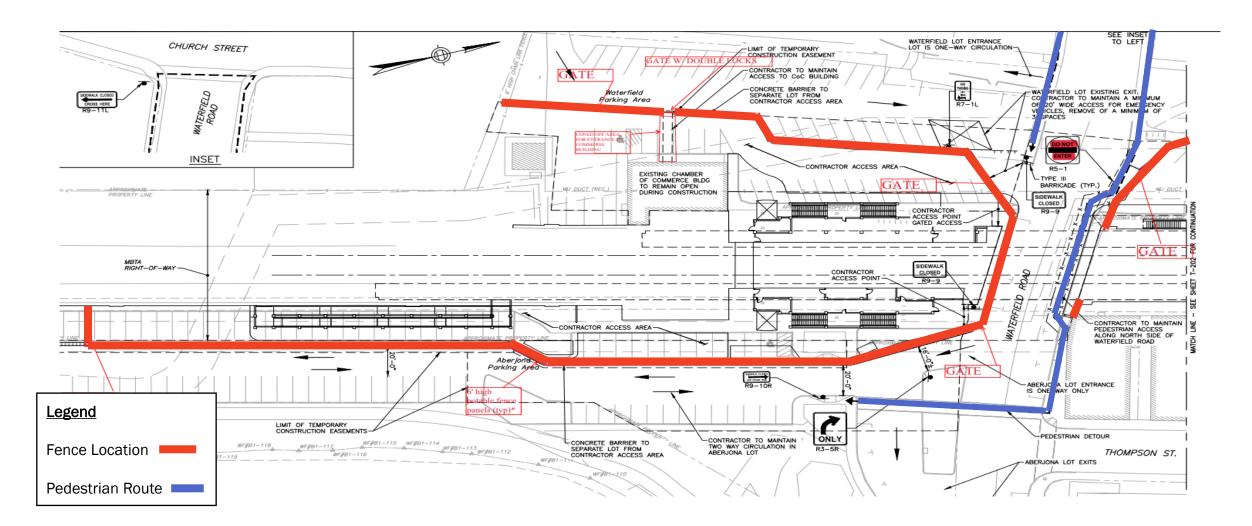

#### **Traffic & Parking Impacts**

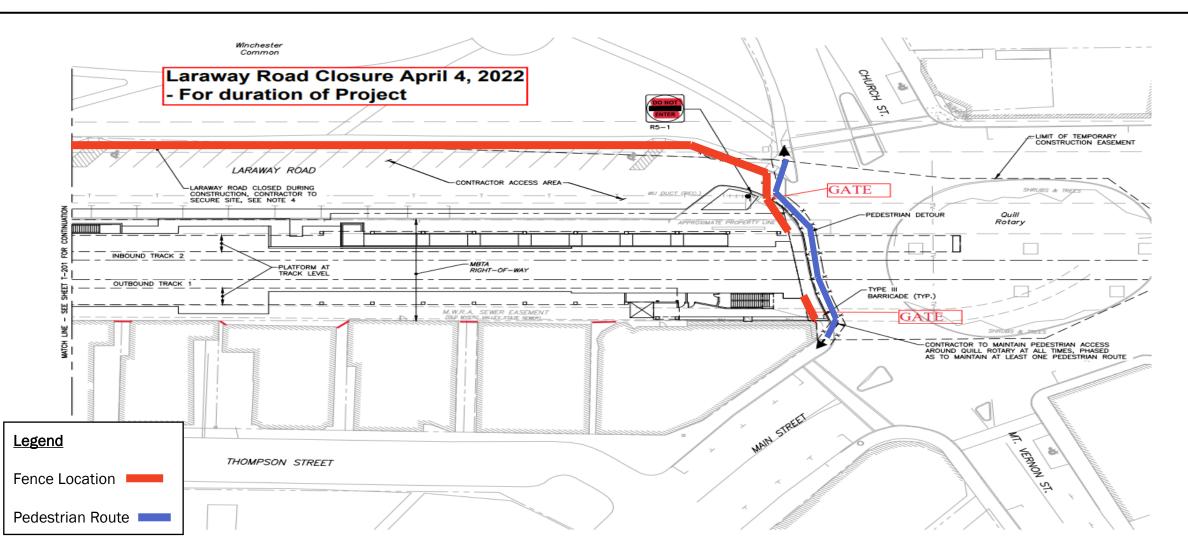


# Parking & Traffic Impacts



- Parking impacts to begin April 4<sup>th</sup>
- Laraway Road will be fenced off and will remain closed for project duration
- Portions of Waterfield Parking Area and Aberjona Parking area unavailable during construction
- Occasional parking & traffic impacts at Waterfield Road

## **Transit Alternatives**

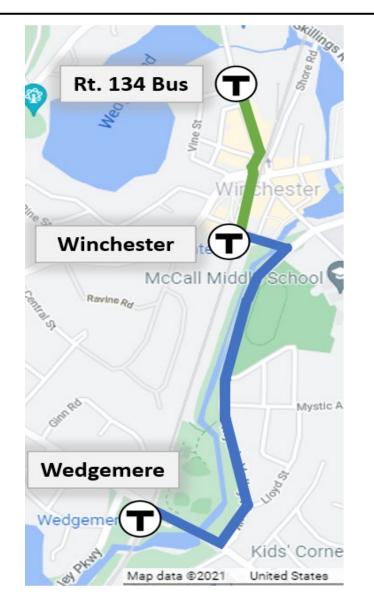

#### Route 134 Bus

- Route 134 Bus to Orange Line (Wellington)
- 0.2 Miles (about a 4-minute walk) from station, shown in green
- Corner of Main Street & Vine

#### **Wedgemere Station**

- 0.7 Miles (about a 3-minute drive) south from Winchester Center, shown in blue
- Walk/bike/drop-off at Wedgemere Station
- Additional bike storage

# Public Outreach

- Upcoming public meeting: Summer 2022
- Project email address: <u>winchesterstation@MBTA.com</u>
- **Construction hotline:** (781) 218-9717 For construction-related concerns and questions.
- Project website:
   <u>www.mbta.com/winchesterstation</u>

