


Week in Review and Lookahead

Friday, March 31, 2023

This past weekend, crews successfully completed the cutover to the new digital signal system between Harvard and Andrew. This weekend, April 1 – 2, [shuttle buses will replace Red Line service between JFK/UMass and Braintree](#) for track and tie replacement



Signal Upgrades

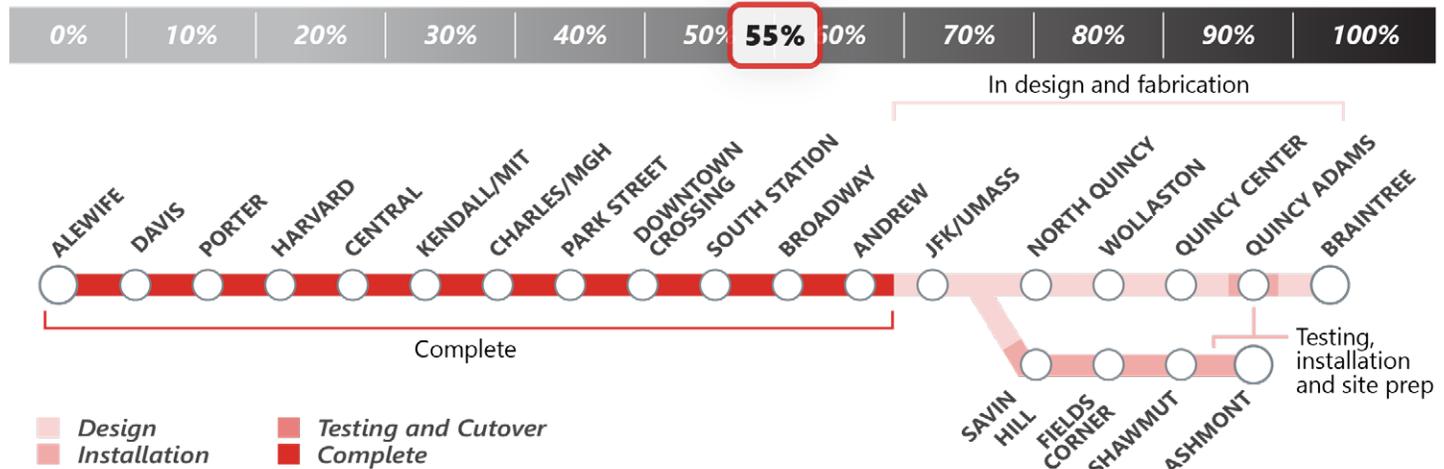

Signal Upgrades: Increase safety and reliability with modernized signals

- ✓ **This Week** | After the successful cutover of the signal system at Central, Park, and Downtown Crossing, crews conducted room clean-up and installed tags. At Quincy Center, crews continued working at the new signal block house preparing the room for signal racks, wires, and cables installation. At Ashmont, crews performed control line testing and installed cases
- **Lookahead** | Crews will continue testing and installing electrical components in preparation of cutovers and diversions

Codman Yard Expansion and Improvements



[Codman Yard Expansion and Improvements](#): Upgrade the yard to increase service capacity, replace outdated infrastructure, and enhance safety

- ✓ **This Week** | Crews continued with job site set-up, routine pest management, installation of the MBTA construction trailer interior, and separation of excavated soil and debris in preparation for disposal
- **Lookahead** | Crews will continue with job site set-up, routine pest management, installation of the MBTA construction trailers, construction survey, clearing vegetation, and excavation of the material stockpile for the new expansion tracks
