



### Week in Review and Lookahead

#### Friday, April 7, 2023

This past weekend, crews worked to replace ties and ballast, then tamped and aligned track on the Braintree branch of the Red Line. Work will continue April 18 – 20, from 8:45 PM to the end of service, when shuttle buses replace [Red Line service](#) from Park Street to JFK/UMass for rail and tie replacement.



### Signal Upgrades

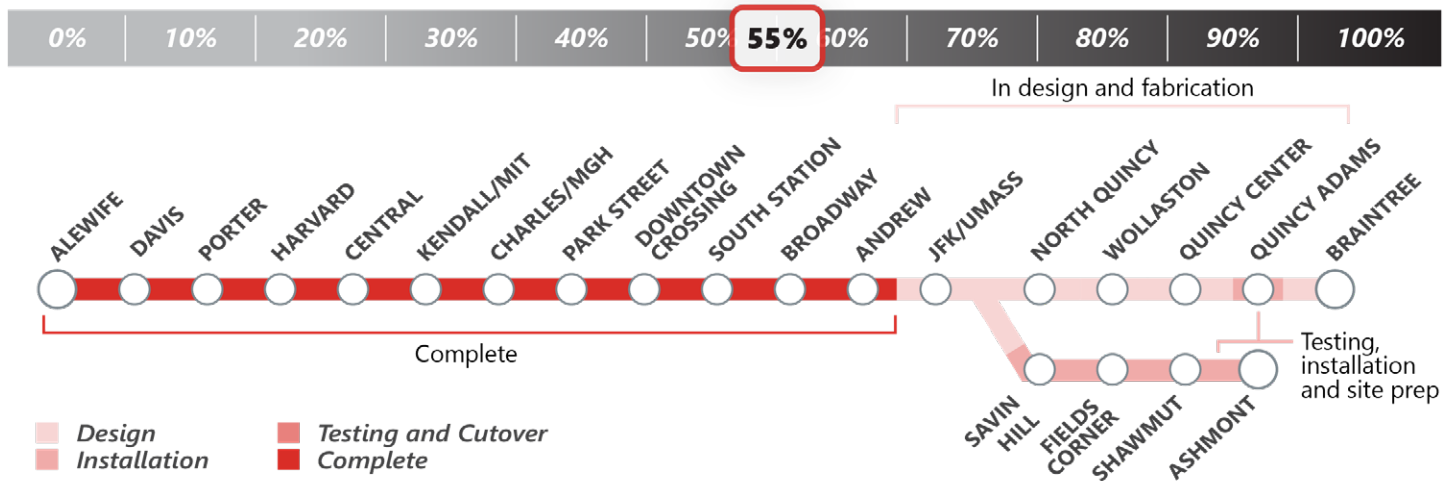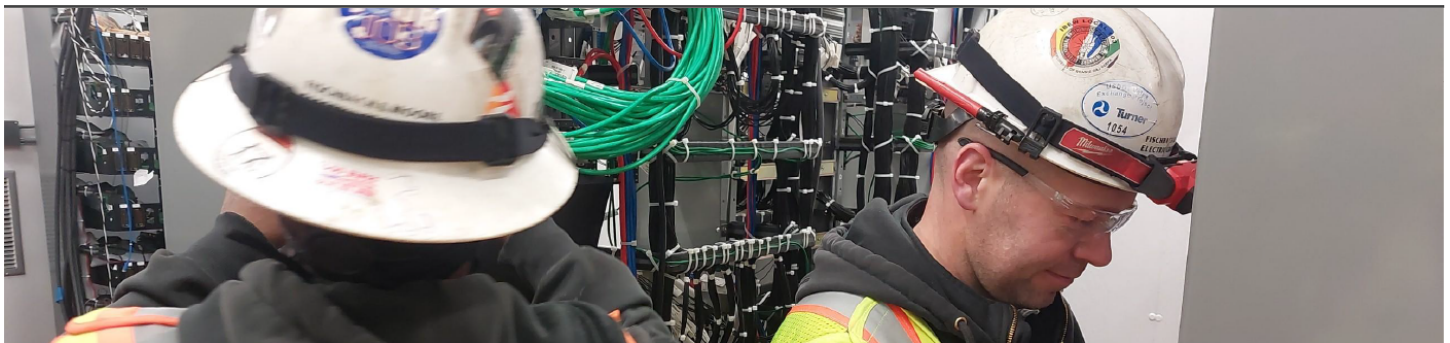

Signal Upgrades: Increase safety and reliability with modernized signals

- ✓ **This Week** | At Ashmont, crews continued system testing. At Quincy Center, crews continued installing new signal racks, wires, and cables. At Quincy Adams, crews performed track circuit testing
- **Lookahead** | Crews will continue testing and installing electrical components in preparation of cutovers and diversions



[Codman Yard Expansion and Improvements](#): Upgrade the yard to increase service capacity, replace outdated infrastructure, and enhance safety

- ✓ **This Week** | Crews continued with job site setup, installation of the MBTA work trailer interior, installation of silt fencing and straw wattles for erosion control, and separation of excavated stockpiled soil from unwanted components
- **Lookahead** | Crews will continue with excavating stockpiled material, clearing trees and vegetation on MBTA property, and surveying to establish elevations for the new storage tracks
