## Green Line Transformation Construction Project Updates




## Week in Review and Lookahead Friday, June 16, 2023

Last weekend, crews replaced over 2,700 feet of rail across the Lechmere Viaduct. Work will continue for the next two weekends, and shuttle buses will replace Green Line service between Union Square and Medford/Tufts and Government Center. **Green Line service** will continue to be suspended between North Station and Government Center until June 25 for work on the Government Center Garage demolition.



## Symphony Station Accessibility Improvements

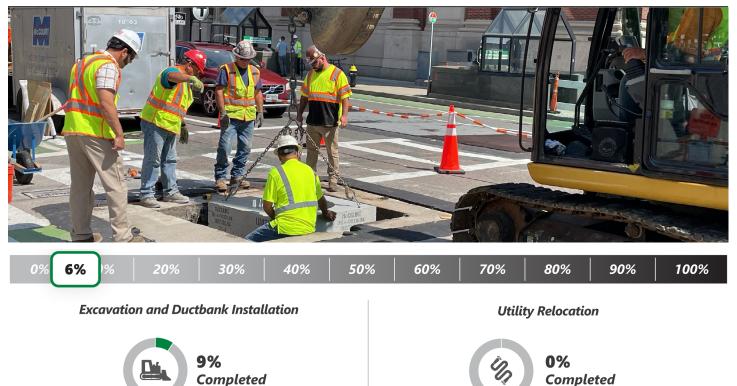

- ✓ This Week | Crews excavated pavement and installed a manhole for cable TV conduit at the Massachusetts Ave/Huntington Ave intersection. Installation of electrical conduit also continued on Huntington Ave and through the underpass
- Lookahead | Work will continue on the cable TV ductbank and crews will begin construction of a ductbank for telephone conduit on Massachusetts Ave between Symphony Towers
