


## Week in Review and Lookahead

### Friday, August 18, 2023

This week, work continued on utility relocation for the Symphony Station Accessibility Improvements project.




### Symphony Station Accessibility Improvements

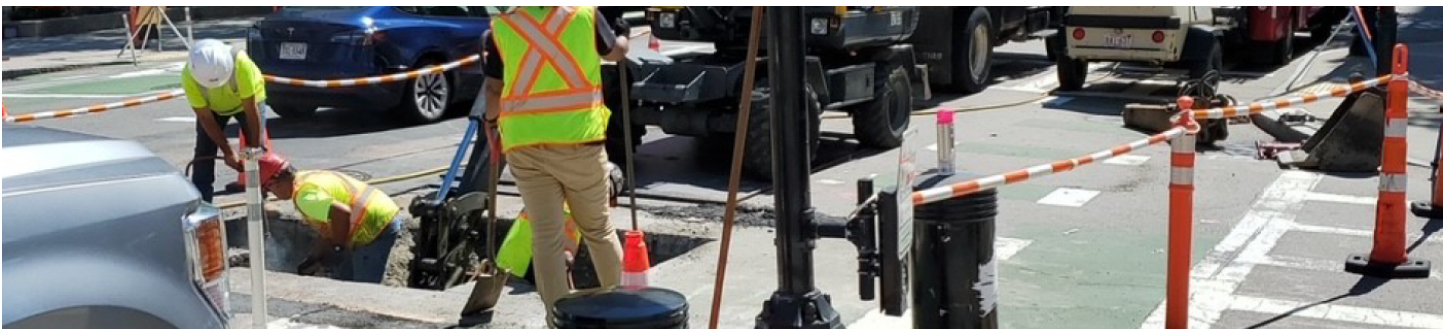

#### Excavation and Duct Bank Installation



#### Utility Relocation



**Symphony Station Accessibility Improvements:** Work to relocate utilities around Symphony Station in advance of work on accessibility upgrades

- ✓ **This Week |** Crews excavated for the cable TV duct bank and manhole, and began placing concrete on a portion of the duct banks for cable TV and telephone (communications) conduit. Contractors connected the new 12" gas line to the existing gas line
- **Lookahead |** Work on communications duct banks will continue
