

# Red Line Transformation

## Construction Project Updates



### Week in Review and Lookahead


Friday, September 8, 2023

This week, the MBTA announced upcoming public meetings for the [Ashmont Branch/ Mattapan Line track upgrades](#) scheduled to take place for 16 days from Saturday, October 14 through Sunday, October 29:

- [Thursday, September 14: 6 PM - 8 PM](#)
- [Tuesday, September 19: 6 PM - 8 PM](#)
- [Wednesday, September 27: 6 PM - 8 PM](#)
- [Saturday, September 30: 1 PM - 3 PM](#)



### Signal Upgrades

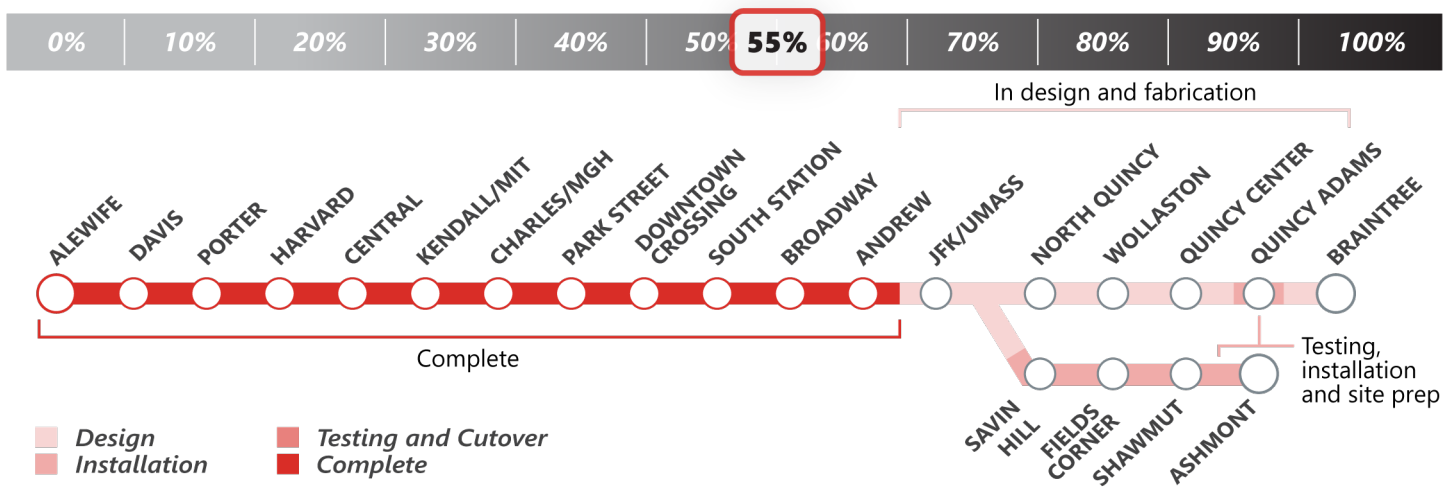

**Signal Upgrades:** Increase safety and reliability with modernized signals

- ✓ **This Week** | Crews prepared for the delivery of the signal house at Columbia Junction this weekend
- **Lookahead** | Material deliveries, work on signal components, and installation are scheduled to take place throughout the Red Line during weekend diversions

\*Schedule subject to change with weather conditions and in accordance with public health directives  
Project percentages represent the value of the installed work

# Codman Yard Expansion and Improvements



## Track Installation




**0%**  
Completed

## Special Track Replacement



**0%**  
Completed

## Traction Power Upgrades



**8%**  
Completed

## Signal Upgrades



**0%**  
Completed

*Codman Yard Expansion and Improvements: Upgrade the yard to increase service capacity, replace outdated infrastructure, and enhance safety*

- ✓ **This Week** | Crews continued excavating trenches, placing new duct banks and backfilling, demolishing bedrock, and managing vegetation
- **Lookahead** | Crews will continue with duct bank installation and vegetation management

# Cabot Yard and Maintenance Facility Updates



## 32,500 Feet of Track



**35%**  
Completed

## 50 Units of Special Track



**34%**  
Completed

## Traction Power & Signals



**32%**  
Completed

*Cabot Yard: Upgrade Cabot Yard to increase service capacity, replace outdated infrastructure, and enhance safety.*

- ✓ **This Week** | Crews excavated and installed duct banks
- **Lookahead** | Crews will continue to excavate and install duct banks for the next several weeks

\*Schedule subject to change with weather conditions and in accordance with public health directives  
Project percentages represent the value of the installed work
