## **Green Line Transformation**

**Construction Project Updates** 




## Week in Review and Lookahead Friday, October 7, 2022

After the successful completion of our first full access closure on the D Branch, work will resume this weekend. From Saturday, October 8 – Sunday, October 16, crews will replace track and upgrade pedestrian crossings at Waban Station, while GLTPS equipment installation continues along the branch.



## **Green Line Train Protection and Track Upgrades**



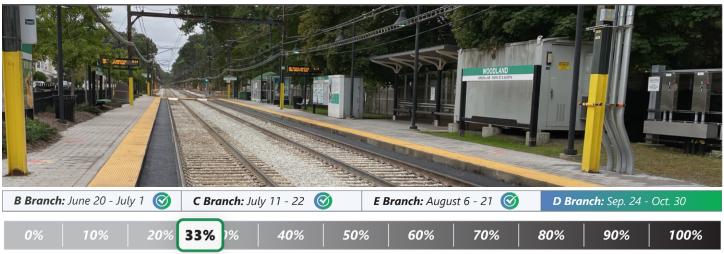

GLTPS Wayside Equipment Installation



25% Completed Track Replacement



**32%**Completed

Pedestrian Crossing Upgrades



**32%**Completed

<u>Green Line Train Protection and Track Upgrades:</u> From June through October, we'll complete over 10,000 feet of track upgrades on the B, C, D, and E branches alongside work on the <u>Green Line Train Protection System (GLTPS)</u>

- ✓ **This Week |** Crews completed work around Woodland Station this past Sunday, October 2 and D Branch service resumed on Monday, October 3
- **Lookahead** | The second D Branch full access closure will take place from Saturday, October 8 to Sunday, October 16. Crews will replace 2,000 feet of rail and upgrade two pedestrian crossings at Waban Station, while installation of GLTPS equipment continues











- ✓ **This Week** | In collaboration with the Town of Brookline, crews began upgrading several pedestrian crossings along Beacon Street on the C Branch. Work began on the Hawes Street crossing and upgrades were completed on the Carlton Street crossing
- **Lookahead** | Work on the Hawes Street crossing will continue next week, and construction will begin on the St. Paul Street crossing
