

# Red Line Transformation

## Construction Project Updates





### Week in Review and Lookahead

#### Friday, April 28, 2023

Crews are continuing to work on removing speed restrictions on the Red Line. Shuttle buses will replace [Red Line service](#) between Kendall/MIT and JFK/UMass this weekend, April 29 – 30, and between Park Street and JFK/UMass next weekend, May 6 -7, for track and tie replacement.



### Signal Upgrades

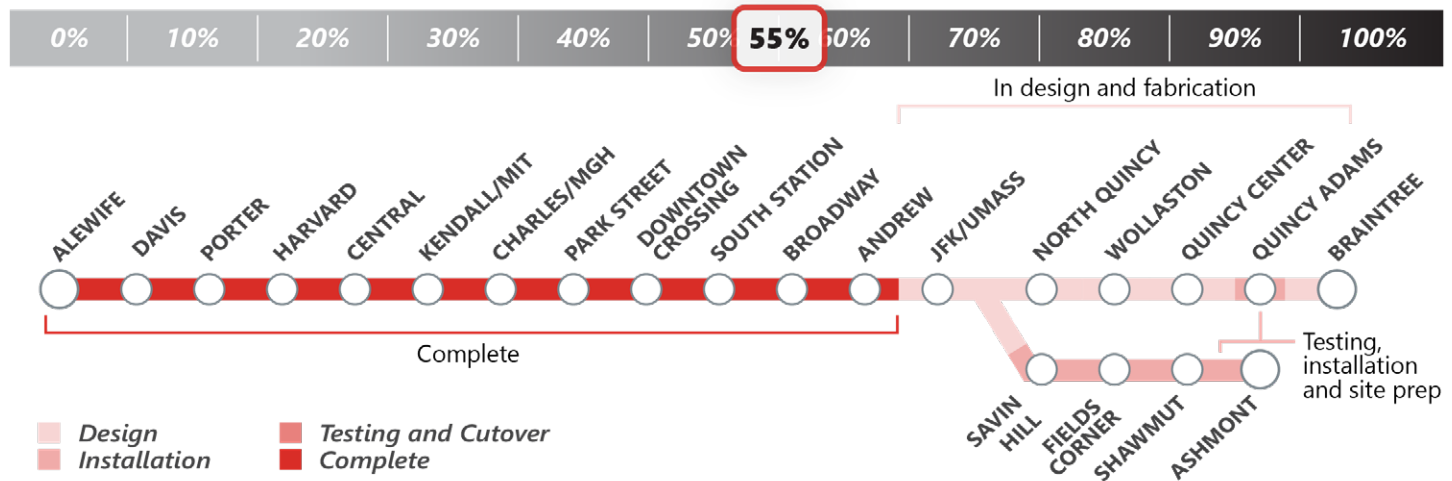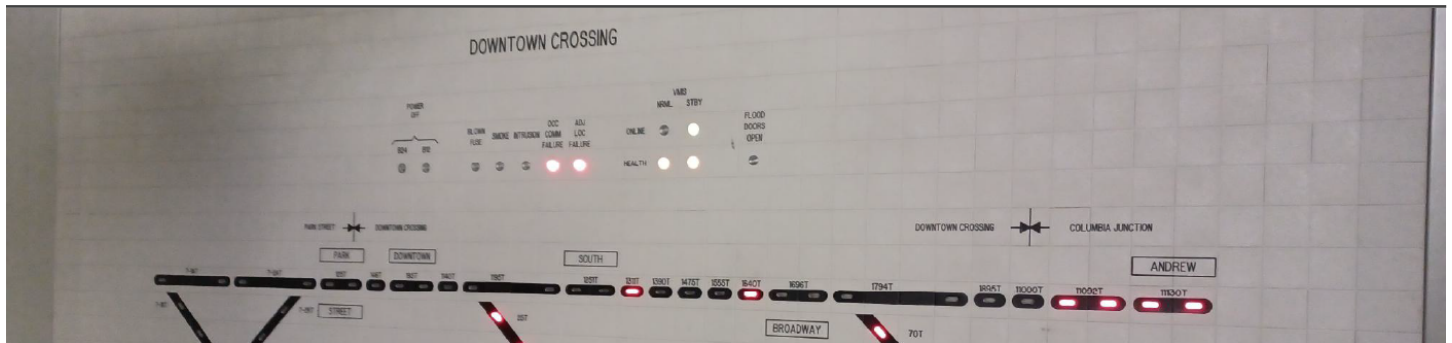

Signal Upgrades: Increase safety and reliability with modernized signals

- ✓ **This Week** | Work is temporarily on hold until further notice due to the prioritization of other work with the MBTA Right-of-Way access

\*Schedule subject to change with weather conditions and in accordance with public health directives  
Project percentages represent the value of the installed work

# Codman Yard Expansion and Improvements



[Codman Yard Expansion and Improvements](#): Upgrade the yard to increase service capacity, replace outdated infrastructure, and enhance safety

- ✓ **This Week** | Crews continued with installation of the MBTA work trailer interior and separation of excavated stockpiled material from unwanted components
- **Lookahead** | Crews will continue excavating and sorting the material stockpile where the new storage tracks will be installed
