


## Week in Review and Lookahead Friday, May 12, 2023

Work is continuing on the removal of Red Line speed restrictions. Rail, track, and tie replacement will continue through the end of May, except for May 15 -18, and May 26 - 29 when work will pause for Memorial Day weekend. Visit the <u>Red Line alerts</u> <u>page</u> to stay up to date on changes to service



## Signal Upgrades

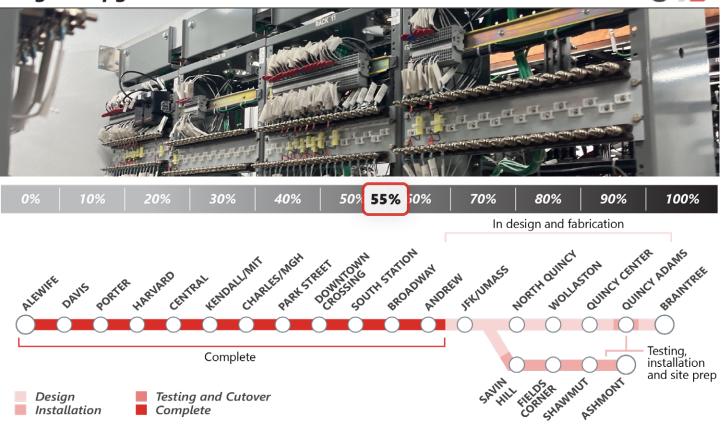

Signal Upgrades: Increase safety and reliability with modernized signals

 This Week | Work is currently on hold until further notice due to prioritization of other work and MBTA Right-of-Way access constraints

## **Codman Yard Expansion and Improvements**



<u>Codman Yard Expansion and Improvements:</u> Upgrade the yard to increase service capacity, replace outdated infrastructure, and enhance safety

- ✓ This Week | Crews continued installing permanent sewer and water systems to the Resident Engineer trailers. Crews excavated for upcoming ductbank placement
- **Lookahead** | Crews will excavate trenches for traction power ductbanks that will be installed under the new storage tracks. The ductbanks provide a protected pathway for buried electrical cables from the substation to the third rail

 $\mathbf{O}$
