
Orange Line Transformation

Construction Project Updates



Week in Review and Lookahead Friday, September 22, 2023

Crews continued to make progress on upgrades to the Orange Line's traction power system and Wellington Vehicle Maintenance Facility this week. Check the <u>alerts page</u> to stay up to date on changes to Orange Line service due to Government Center Garage demolition.



Wellington Maintenance Facility Updates





Building Upgrade



92%Completed

Power Substation



98% Completed Train Wash



92%Completed

Maintenance Bays




80%Completed

<u>Wellington Maintenance Facility:</u> Modernize the Vehicle Maintenance Facility to improve vehicle maintenance, reduce downtime and customer wait times, provide cleaner trains, and deliver safer operations

- ✓ This Week | Crews worked to install new floor drains at tracks 12 and 13. The train wash system was tested
- **Lookahead** | Crews will continue installing floor drains at tracks 12 and 13. Electrical updates will continue within the building, and the train wash will be brought into service

Traction Power Substations



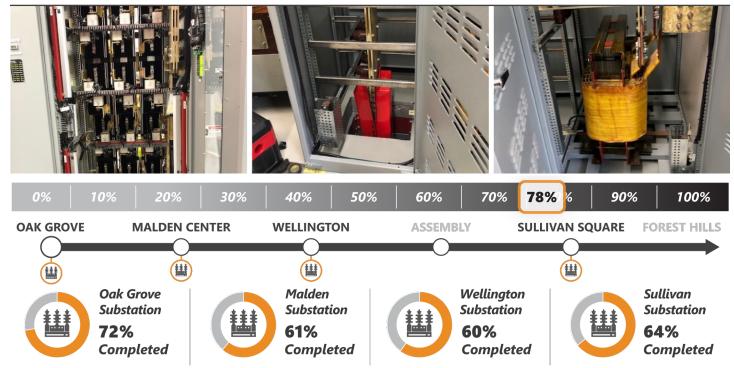

<u>Traction Power Substations:</u> Modernize the third rail power supply to reduce the risk of service disruptions; develop a power system capable of supporting additional Orange Line service

- ✓ **This Week** | At Oak Grove, crews continued working on electrical connections at transformer 2, performing testing, wiring switchgear, and cutting conduits. At Sullivan, crews conducted testing at the substation
- **Lookahead** | Crews will continue performing cable connections, installing electrical connections, and testing new equipment
