

Week in Review and Lookahead

Friday, September 22, 2023


The MBTA is holding two more public meetings to discuss the upcoming [Ashmont Branch/Mattapan Line track upgrades](#) scheduled to take place from Saturday, October 14 through Sunday, October 29:

- [Wednesday, September 27: 6 PM - 8 PM](#)
- [Saturday, September 30: 1 PM - 3 PM](#)

Check the [alerts page](#) to stay up to date on changes to Red Line service




Signal Upgrades

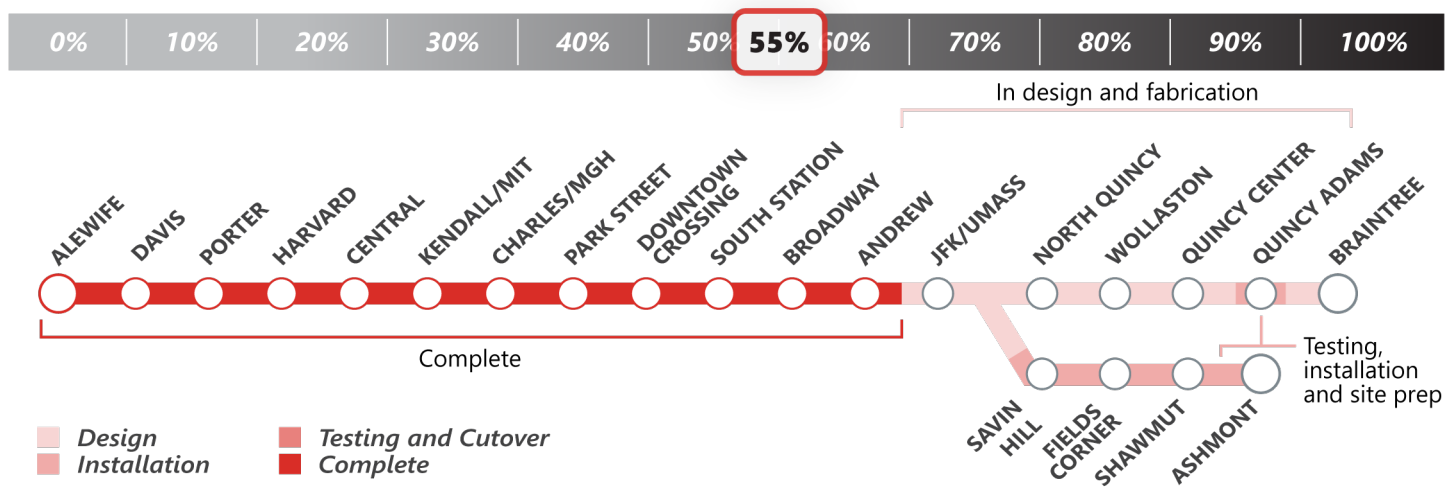

Signal Upgrades: Increase safety and reliability with modernized signals

- ✓ **This Week** | No work was scheduled for this week
- **Lookahead** | Deliveries, installation, and testing of signal components and materials are scheduled for upcoming weekend diversions on the Red Line


Codman Yard Expansion and Improvements

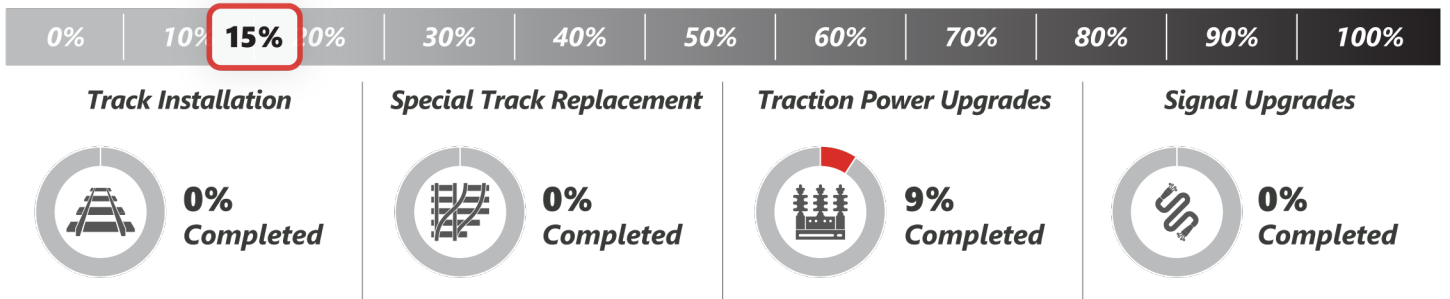

Codman Yard Expansion and Improvements: Upgrade the yard to increase service capacity, replace outdated infrastructure, and enhance safety

- ✓ **This Week** | Crews continued working at Zone A by excavating trenches, placing concrete for new duct banks and backfilling, drilling rock, and conducting borings
- **Lookahead** | Crews will continue with duct bank installation and borings

Cabot Yard and Maintenance Facility Updates

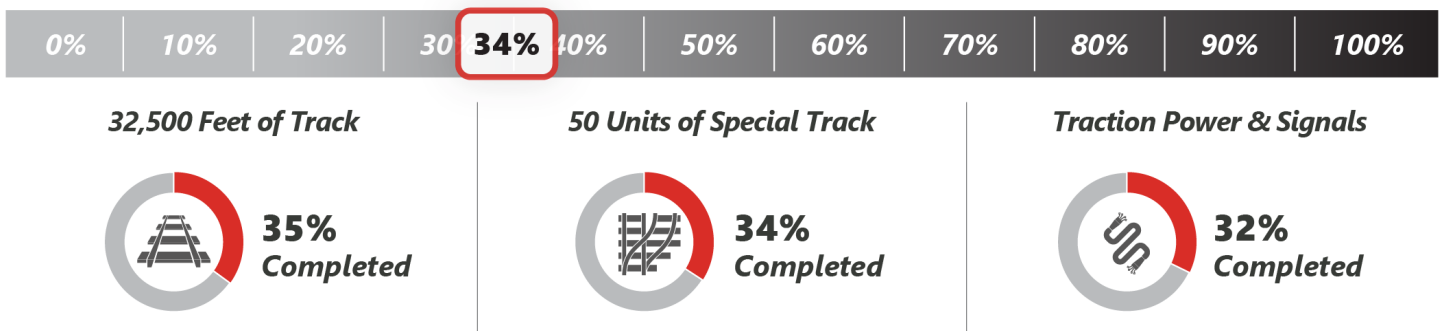

Cabot Yard: Upgrade Cabot Yard to increase service capacity, replace outdated infrastructure, and enhance safety.

- ✓ **This Week** | Crews prepared for a concrete pour by installing conduit, rebar, and formwork for the traction power duct banks
- **Lookahead** | The excavation and installation of duct banks will be ongoing for the next few weeks

*Schedule subject to change with weather conditions and in accordance with public health directives
Project percentages represent the value of the installed work
