



Green Line Extension Update

January 14, 2019



massDOT
Massachusetts Department of Transportation




Agenda

- Project Controls
- Design Status
- Construction Progress and Planning
- Outreach








Initial Performance Indicator – Dashboard Graphics

Design Build (DB) Entity Contract Cash Flow Performance

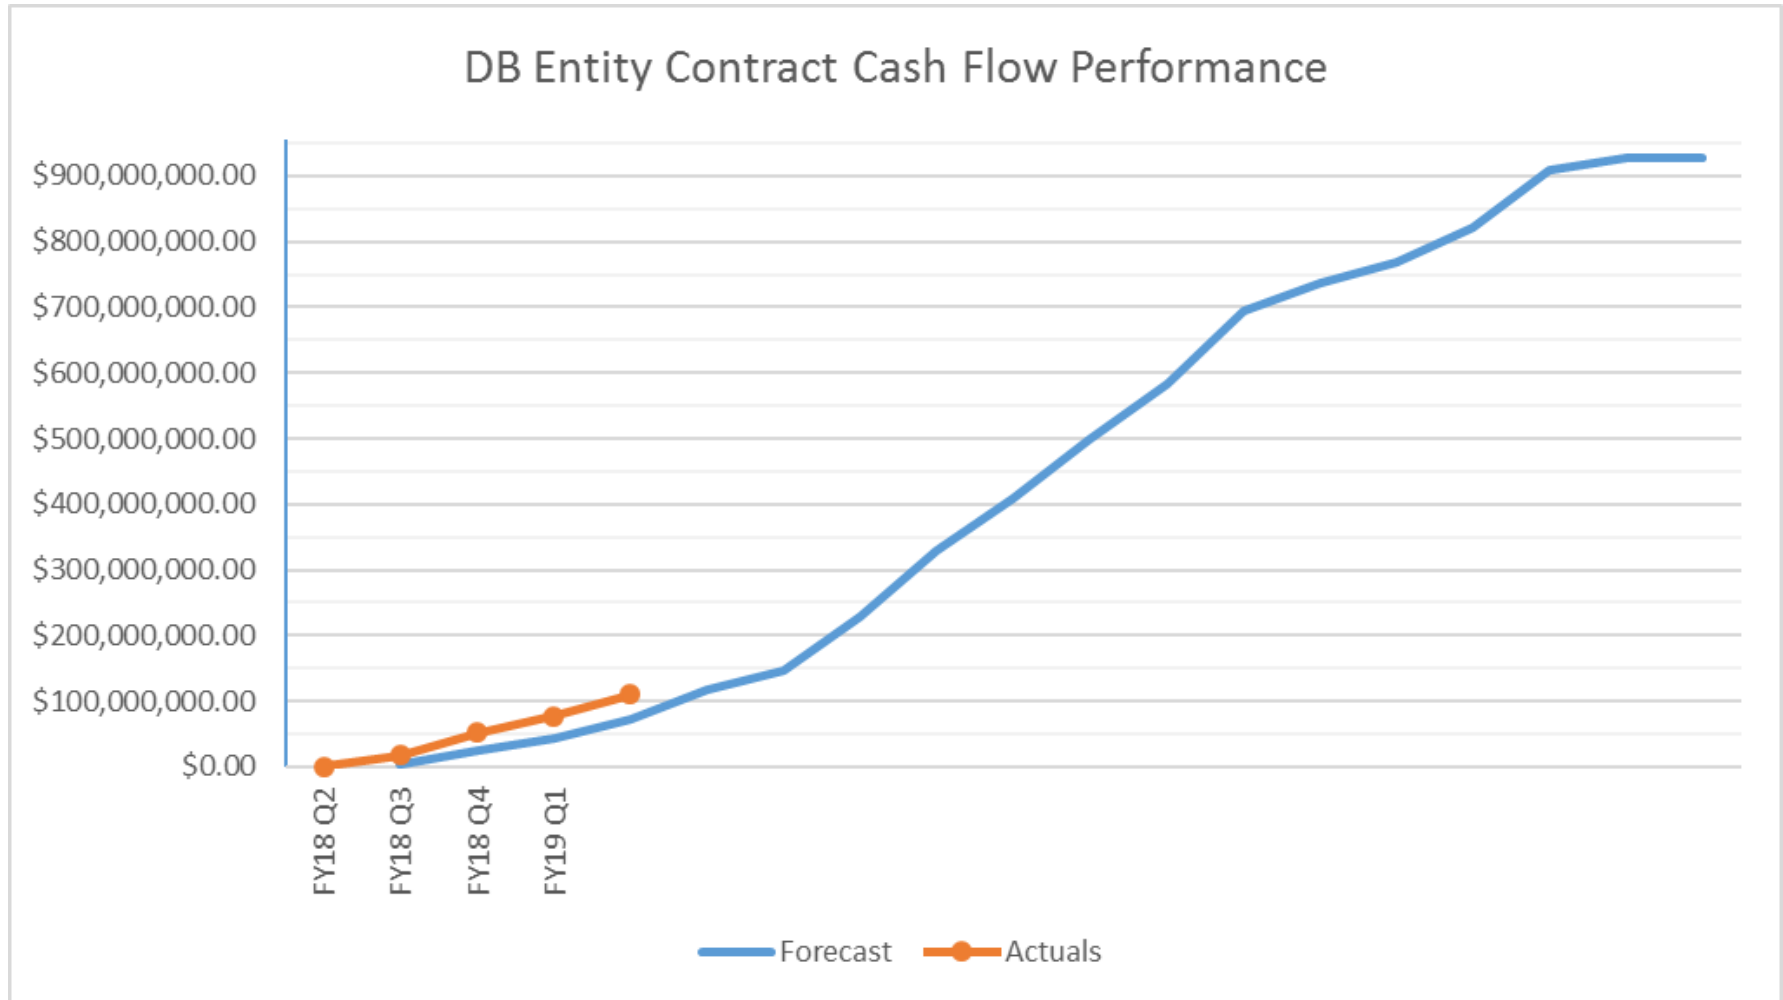

Initial Performance Indicator – Dashboard Graphics

Design Station Progress Update*

		% Complete	
		Mar 2018	Dec 2018
• Lechmere		10%	76%
• East Somerville		0%	23%
• Gilman		30%	80%
• Magoun		0%	44%
• Ball Square		0%	45%
• Union Square		0%	24%
• College Ave.		5%	75%

**D
E
S
I
G
N**

***Average design completion status across 58 total design packages = 60%**

Construction Progress & Planning

- Building demolition to commence in January
- Viaduct substructure mobilization underway
- Drainage infrastructure installation underway
- Retaining wall and noise wall construction underway




Construction Progress & Planning

Staffing

- GLX/MBTA personnel including consulting staff 95
- GLXC personnel including subcontractor staff 225

320+/- Total FTEs

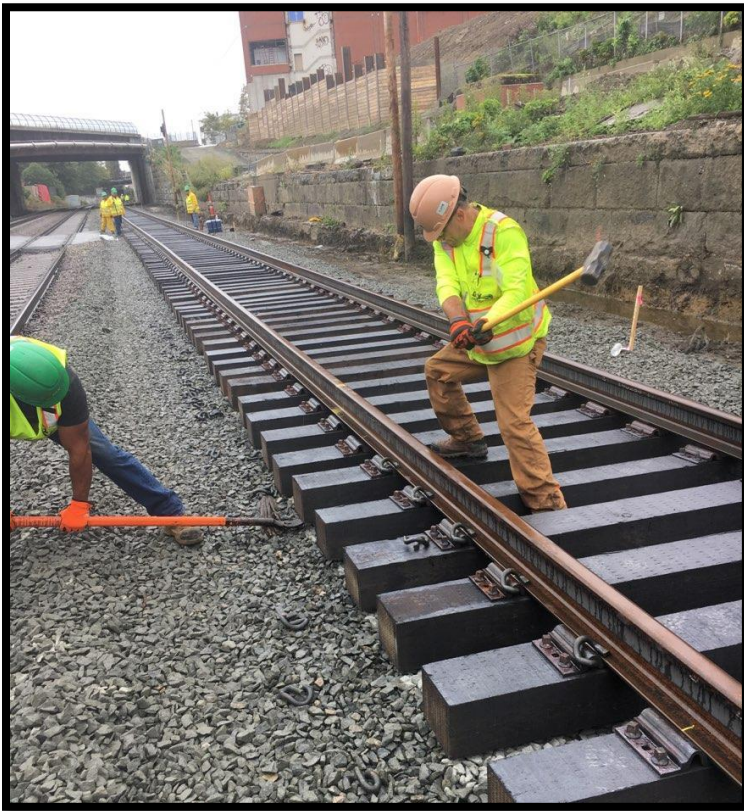

massDOT
Massachusetts Department of Transportation



Broadway Bridge Closure Update

Bridge Demolition & Construction

- Target start date - March 2019 for bridge closure
- 12 month demolition and construction schedule




Washington St. Bridge Update

Closure Dates:

Phase I Closure: April 2019 to November 2019

Phase II Closure: Spring to Fall 2020

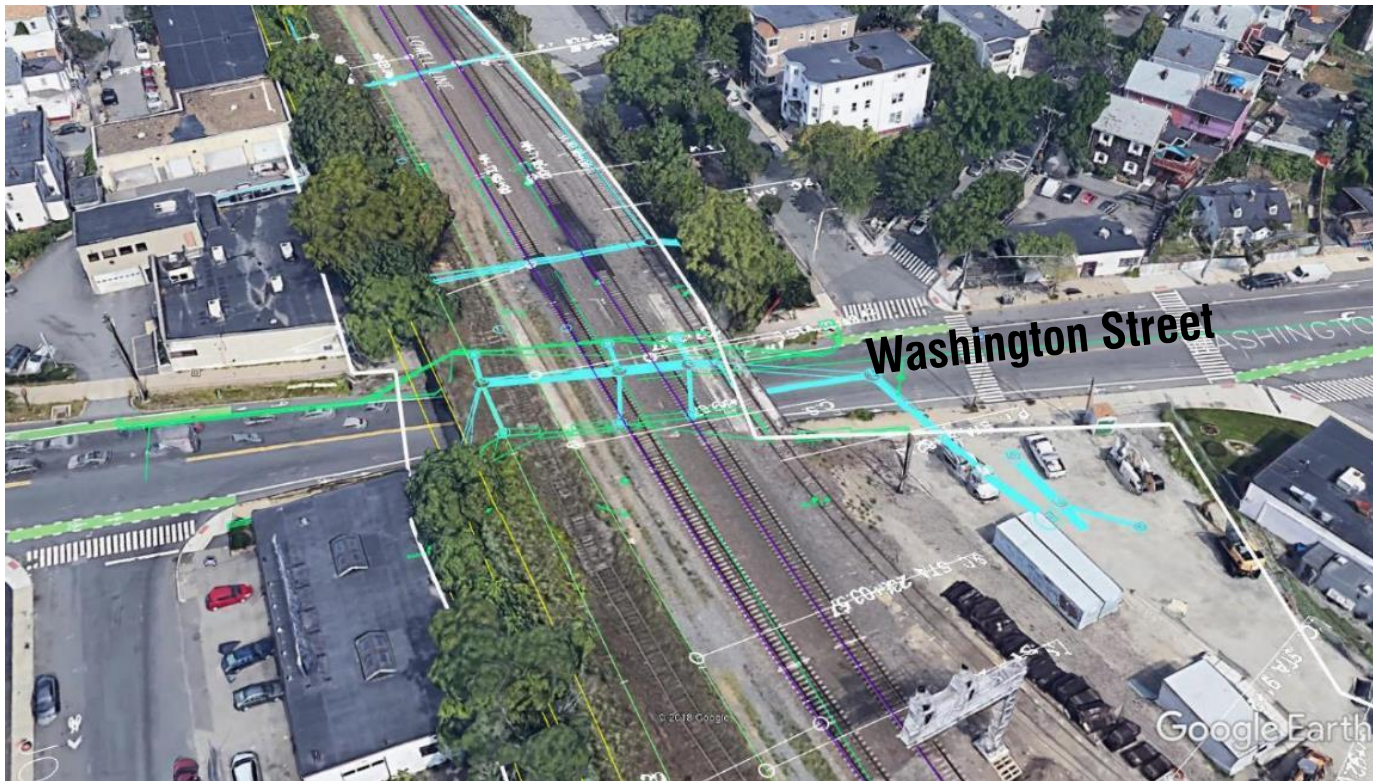

massDOT
Massachusetts Department of Transportation



MBTA Bus Routes

Bridge Closure	Route #	Description	Trip-Time Impact
Broadway	80	Arlington Center - Lechmere	5 – 15 Minutes
Broadway	86	Sullivan - Reservoir	5 – 15 Minutes
Washington Street	89	Clarendon Hill or Davis - Sullivan	5 – 10 Minutes
Washington Street	91	Sullivan – Central Sq. - Cambridge	5 – 10 Minutes
Washington Street	CT2	Sullivan - Ruggles	5 – 10 Minutes



Regional Outreach

Target Audience	Tactics/Approach
<ul style="list-style-type: none">• Commuting Public• Neighboring City/Town Municipalities• Media Outlets• Hospitals and Medical Facilities• Colleges/Universities/Schools• Chamber of Commerce & Large Employers	<ul style="list-style-type: none">• Variable Message Signs (VMS)• Email Blasts (More than 6300 registered)• MassDOT Social Media• Public Service Announcements• Municipal Websites• News Media Engagement



Local Outreach

- Community Working Group (14 consecutive monthly meetings)
- GLX website updates
www.mass.gov/green-line-extension-project-glx
- Email Blasts (>6300 registered)
- Automated phone calls
- Door-to-door leafletting
- Public Meetings (next is Jan. 30th)
- City Traffic Engineers & First-Responders
- Tabling Events (16 events, 2200 engagements)



Outreach

Upcoming Events

➤ Next Public Meeting

Wednesday, January 30, 2019

6:00 – 8:00 p.m.

East Somerville Community School

50 Cross Street, Somerville, MA 02145




Outreach

GLX Community Connection Team – Holiday Drive

- **Somerville Homeless Coalition (Project Soup)**
 - *Non-perishable food & hygiene items*
- **Medford Family Network**
 - *Clothing & Toy Drive*
- **Cambridge Youth on Fire**
 - *Delivered meals for young people*

Outreach

GLX Team Donated and Delivered 800 lbs. of Product

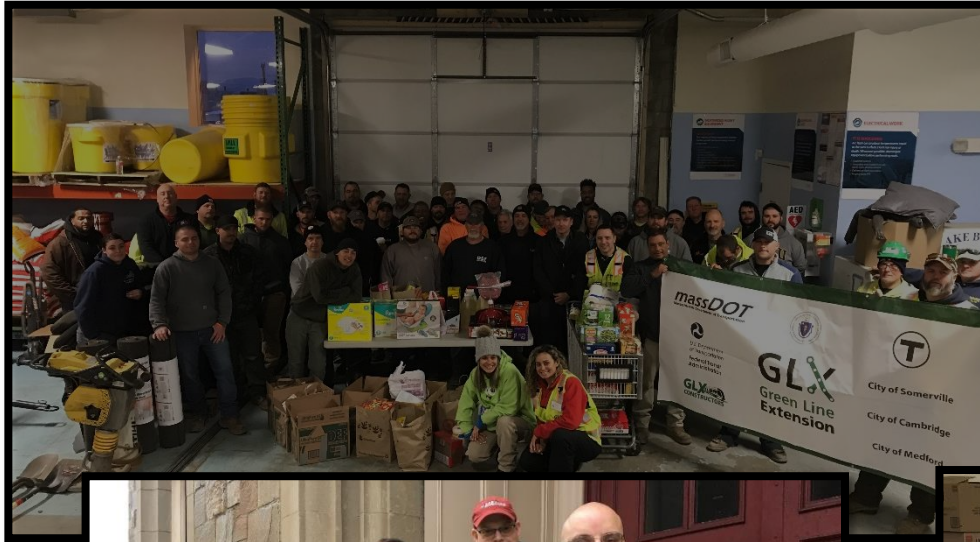



Green Line Extension Update

January 14, 2018

